BRUHATH BANGALORE MAHANAGARA PALIKE,

Name of Work: Providing Sinking of Borewell drilling and pumps in Dasarahalli ward no 15.

Sl No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
1	Geophysical survey geophysical investigation of site for sinking Borewell for supplying drinking water to the habitation either through the hand pumps, MWS or PWSS by vertical electrical sounding by adopting venner or schlumbergers's method including recconnaisance suevey of geological formation Geophysical investigation of existing ground Water in the vicinity. its quality , quality & acceptabality of the users indicating the location of the site recommendeddepth of casing pipe required to seal the tope unconsolidated formation including an extra depth 1.0 metre in consolidated formation for aquire proposed to be tapped propable yield and other information required including transportation of instrument and accessories to work site, engating technical personal and labour etc., **(SR RDWS&S 2019-20, Page No-148 , Item No-13.04)**								
	Krishnegowda Layout 1st Main	Each	1				1.00		
	K K Road Near Masjid		1				1.00		
	Buvaneshwari nagar 3rd Main		1				1.00		
							3.00	**3918.72**	**11756.00**
	Assistant Engineer 05/04/21 Ward 15							Assistant Executive Engineer Dasarahalli Sub Division, BBMP	
2	Sinking of Borewell of 165 mm clear using fast hydraulic rig of capacity 250 PSIG & above 900 CMF & abpve in al strata including over burden upto 22 m fixing of casing pipes, collars and cap with necessary cutting and threading including transporation of rig and surpporting vehicles, screws charges and cost of consumable including yield testing at the final depth with a minimum working of compressor for one hour all as specified., (SR RDWS&S 2019-20, Page No- 148,Item No-13.01 (a to i)								
	0.00 To 50.00 mtr	Rmtr							
	Krishnegowda Layout 1st Main		1	50.00			50.00		
	K K Road Near Masjid		1	50.00			50.00		
	Buvaneshwari nagar 3rd Main		1	50.00			50.00		
							150.00	**360.88**	**54132.00**
	50.00 to 100.00 mtr								
3	Krishnegowda Layout 1st Main		1	50.00			50.00		
	K K Road Near Masjid		1	50.00			50.00		
	Buvaneshwari nagar 3rd Main		1	50.00			50.00		
							150.00	**459.68**	**68952.00**
	100.00 to 150.00 mtr								

Scanned with CamScanner

Sl No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
	Krishnegowda Layout 1st Main		1	50.00			50.00		
4	K K Road Near Masjid		1	50.00			50.00		
	Buvaneshwari nagar 3rd Main		1	50.00			50.00		
							150.00	474.24	71136.00
	150.00 To 200.00 mtr								
	Krishnegowda Layout 1st Main		1	50.00			50.00		
5	K K Road Near Masjid		1	50.00			50.00		
	Buvaneshwari nagar 3rd Main		1	50.00			50.00		
							150.00	557.44	83616.00
	200.00 to 250.00 mtr								
	Krishnegowda Layout 1st Main		1	50.00			50.00		
6	K K Road Near Masjid		1	50.00			50.00		
	Buvaneshwari nagar 3rd Main		1	50.00			50.00		
							150.00	659.36	98904.00
	250.00 to 300.00 mtr								
	Krishnegowda Layout 1st Main		1	50.00			50.00		
7	K K Road Near Masjid		1	50.00			50.00		
	Buvaneshwari nagar 3rd Main		1	50.00			50.00		
							150.00	728.00	109200.00
	300.00 to 350.00 mtr								
	Krishnegowda Layout 1st Main		1	50.00			50.00		
8	K K Road Near Masjid		1	50.00			50.00		
	Buvaneshwari nagar 3rd Main		1	50.00			50.00		
							150.00	858.00	128700.00
	350.00 to 400.00 mtr								
	Krishnegowda Layout 1st Main		1	50.00			50.00		
9	K K Road Near Masjid		1	50.00			50.00		
	Buvaneshwari nagar 3rd Main		1	50.00			50.00		
							150.00	936.00	140400.00

Assistant Engineer
Ward 15
09/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Scanned with CamScanner

Sl No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
10	Providing and Fixing 250mm dia PVC pipe and as per Specification and Direction								
	Krishnegowda Layout 1st Main	Rmtr	1	25			25.00		
	K K Road Near Masjid		1	25			25.00		
	Buvaneshwari nagar 3rd Main		1	25			25.00		
							75.00	1189.76	89232.00

Assistant Engineer
Ward 15
10/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

11	Supply of ISI Mark nominal bore, plain end **steel casing pipe**-grade of steel Fe 410 of wall thickness conforming to IS 4270-2001 and latest amendments, electrical resistance welded steel tube material and conforming to IS 1387- 1993 and manufactured by basic open hearth electric or basic oxygen process in random length of 5 to 7m. Both ends threaded conforming to IS 554-1985, one end fixed with socket conforming to IS 4270-2001 and the other end with screwed pipes. All pipes shall be resonably free from defects. The tubes shall be resonably straight and should be with ISI marking weighing 25.10kg/m. **(SR RDWS&S 2019-20, Page No-338 , Item No-15.85)**								
	Krishnegowda Layout 1st Main	Rmtr	1	200			200.00		
	K K Road Near Masjid		1	200			200.00		
	Buvaneshwari nagar 3rd Main		1	150			150.00		
							550.00	1378.00	757900.00

Assistant Engineer
Ward 15
10/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

12	Providing and fixing **MS casing collars** as per IS 1239 (part-II) 1982 with all latest amendments if any for any dia. The thickness of plate used for covering one end shall be 3mm (minimum). The dimensions of caps and colars shall be strictly as per IS 1239 (Part-II) 1982 with all amendments **(SR RDWS&S 2019-20, Page No-338 , Item No-15.86)**								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	156.00	468.00

Assistant Engineer
Ward 15
10/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Scanned with CamScanner

Sl No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
13	Providing and laying at site of work MS casing caps as per IS 1239 (part-II) 1982 with all latest amendments if any for any dia. The thickness of plate used for covering one end shall be 3mm (minimum). The dimensions of caps and colars shall be strictly as per IS 1239 (Part-II) 1982 with all amendments including cost of material and labour charges for fixing, if any etc. complete with all lead and lifts and as directed by the Engineer in charge **(SR RDWS&S 2019-20, Page No-338 , Item No-15.86)**								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Main		1	1.00			1.00		
							3.00	**104.00**	**312.00**
14	Supplying and delivery of Submersible Pump Sets of 150mm dia suitable for bore well and confirming to IS 8034 specifications and its latest ammendments, 3-Phase, SS Bowl and impeller with low volt motor with testing as per instructions of Engineer incharge of work. (15 HP STG)**(SR PWD 2018-19 P. No. XLII/44)**								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	**70433.00**	**211299.00**
15	Supplying, laying, jointing testing and commissioning of GI pipes confirming to IS 1239:1990 with latest amendments, including fising collars, Elbows, Tees, bends, Glad Cocks and other Fittings (Excluding Cost of Specials) with Cuts and Threads wherever necessary including conveying the materials to workspot, including testing for water tightness with all lead and lifts etc complete (Contractor shall make his own arrangements for procuring water for testing) Class-C -Heavy 50mm Dia **(SR RDWS&S 2019-20 Pg No.93 I No.10.04.03 (f))**								
	Krishnegowda Layout 1st Main	Rmtr	1	300.00			300.00		
	K K Road Near Masjid		1	300.00			300.00		
	Buvaneshwari nagar 3rd Main		1	300.00			300.00		
							900.00	**481.52**	**433368.00**

Assistant Engineer
Ward 15
16/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP
ಟಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಿಬಿಎಂಪಿ, ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

Sl No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
16	Suppy and fixing 50mm dia GI collar Heavy duty (SR PWD 2018-19 pg no. XLVII/2)								
	Krishnegowda Layout 1st Main	No	1	60.00			60		
	K K Road Near Masjid		1	60.00			60		
	Buvaneshwari nagar 3rd Main		1	60.00			60		
							180.00	187.20	33696.00
17	Supplying and drawing 3 core flat PVC sheathed submersible pump cable manufactured with electrolytic grade copper with flexible copper with low resistance conductor confirming to IS:8130-1984 and virgin grade PVC insulation and powder coating extruded PVC sheathed suitable for working voltage upto 1100Volts as per IS-694:1990.3C X 6.0Sq.mm **(ELECTRICAL SR 2019-20 P-07/I. NO 2.6.4**								
	Krishnegowda Layout 1st Main	Rmtr	1	600			600		
	K K Road Near Masjid		1	600			600		
	Buvaneshwari nagar 3rd Main		1	600			600		
							1800.00	246.50	443700.00
18	Supply and delivery at site of brand new best make non-return valve as per IS 778/1984 With ISI Mark and as per its latest amendments 50mm Dia **(SR RDWS&S 2019-20, Pg No 129 Item No.12.06 (a))**								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	1222.00	3666.00

Assistant Engineer
Ward 15
16/04/21

Assistant Executive Engineer
T.Dasarahalli Sub Division, BBMP
ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಜಿ.ಜಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Assistant Engineer
Ward 15
19/04/21

Assistant Executive Engineer
T.Dasarahalli Sub Division, BBMP
ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಜಿ.ಜಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Assistant Engineer
Ward 15
19/04/21

Assistant Executive Engineer
T.Dasarahalli Sub Division, BBMP
ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಜಿ.ಜಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
9	Supplying and delivery at site brand new star/Essen/Lotus/Sun-Shines/Adarsh/ G.K.Controls Best Indigenous make combined energy meter-cum-control panel board unit minimum mechanically strong suitable for operation on 3HP 50HZ 380/440 Volts AC supply with spring loaded latch locking Device with a key Ribbs should be provided. contron panal board unit suitable for operation on 3HP 50HZ 380/440 Volts AC shall be consists Etc. complete the panal board shall be fabricated in single unit in the above components panal board suitable pump set 10HP to 20HP with stae delta starter out door panel board up to 20HP **(SR PWD 2018-19 P. No. XLVII/13)**								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	**21840.00**	**65520.00**

Assistant Engineer
Ward 15
23/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

20	Labour charges for Erection, Electrification and commissioning of Pump sets, including aligning and balancing of all items including supply and erection of two pair of supporting clamps, bore well caps, cable clips and water tight gland cable protectors, bolts, nuts, valve and gauges,tools and equipments etc., involved in the job as per specifications, with necessary tests as per specifications, with testing of as per instructions of engineer incharge of work.**(SR RDWS&S 2019-20, Pg No.130 I No. 12.16)**								
	Krishnegowda Layout 1st Main	Job	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	**5876.00**	**17628.00**

Assistant Engineer
Ward 15
26/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

21	Labour charges for erection of outdoor type panel board and meter board units with all necessary materials and labour, tools and equipments including providing cement concrete foundation bed etc., complete as per specification, with testing of as per instructions of engineer incharge of work. **(SR RWDS 2019-20, Pg No.131, I No. 12.18)**								
	Krishnegowda Layout 1st Main	Job	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	**1245.92**	**3738.00**

Assistant Engineer
Ward 15
26/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Scanned with CamScanner

Sl No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
22	Supplying of TPST with rewirable porcelain channels in SM enclosure 32 amps (Ele SR 2019-20 P-NO24/ I/NO 5.5.1)								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	1872.00	5616.00
23	Supply and fixing polished wood board made of not less than 15mm thick plank on both sides of not more than 2 pieces and fixing the same to the wall using tapered inverted wooden plugs crews.20"x20"x2.5" (Ele SR 2019-20 P-NO24/ I/NO 5.6.6)								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	303.68	911.00
24	Supplying and fixing of LED type panel board indicating lamp with required colour suitable for 230/440v A.C. 50 Hz 12/24v D.C.(Ele SR 2019-20 P-NO29/ I/NO 5.38)								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	447.20	1342.00
25	Supplying, fixing and wiring heavy duty low voltage capacitors conforming to IS 2834. 3 phase, 400/440 volts grade, for power factor improvement of rotating machineries like induction motor. 2KVAR (Ele SR 2019-20 P-NO29/ I/NO 5.37)								
	Krishnegowda Layout 1st Main	KVAR	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	416.00	1248.00

Assistant Engineer
Ward 15
29/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP
ಬೆಂಗಳೂರು-560073

Assistant Engineer
Ward 15
29/04/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP
ಬೆಂಗಳೂರು-560073

Assistant Engineer
Ward 15
10/05/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP
ಬೆಂಗಳೂರು-560073

Assistant Engineer
Ward 15
10/05/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
26	Supplying and fixing miniature circuit breakers on existing MCB distribution boards using necessary fixing materials and 'C' Type curve, indicator ON/OFF, energy cross-3 with Short circuit breaking capacity of 10K and complete wiring as required confirming to IEC 60898. 6 to 32amps **(Ele SR 2019-20 P-NO27/ I/NO 5.17.7)**								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	**1783.60**	**5351.00**

Assistant Engineer
Ward 15
17/05/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

27	Supplying, fixing, wiring, earth electrode for grounding conduits, I.C. cutouts and other equipment's on the meter board using 40mm dia 2.90mm thick GI pipe 2.5 mtr long buried in a pit ... The pit should be filled with equal proportion of salt and charcoal 150mm all-round the pipe to complete depth. The connection from the pipe to the conduit etc., is to be established through GI wire of size as per ISI specification 7.3.3. of IS 732 using 12mm dia bolts, nuts, washers and check nuts etc., the pipe shall have 16 through holes of 12 mm dia **(Ele SR 2019-20 P-NO40/ I/NO 6.1)**								
	Krishnegowda Layout 1st Main	No	1	1.00			1.00		
	K K Road Near Masjid		1	1.00			1.00		
	Buvaneshwari nagar 3rd Main		1	1.00			1.00		
							3.00	**3119.69**	**9359.00**

Assistant Engineer
Ward 15
17/05/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

	Supplying and fixing of class A (medium duty) GI pipe of wall thickness not less than 3.25mm on pole/wall/drain crossing with necessary clamping arrangements for UG cable of 1.1 KV class 40mm dia **(Ele SR 2019-20 P-NO41/ I/NO 6.9.1)**								
	Krishnegowda Layout 1st Main	Rmt	1	3.00			3.00		
	K K Road Near Masjid		1	3.00			3.00		
	Buvaneshwari nagar 3rd Main		1	3.00			3.00		
							9.00	**348.40**	**3136.00**

Assistant Engineer
Ward 15
21/05/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Scanned with CamScanner

Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
Supplying of 1.1 KV LT UG cable XLPE or Heat resistant PVC insulated, PVC extruded Inner sheath armoured UG LT cable as per IS-1554 (Part-1) or IS-7098 Part-1, Armouring strip thickness in average +5% and resistivity 14 Ohms/Kms (Max) as per IS-3975 **(Ele SR 2019-20 P-NO40/ I/NO 6.4.4)**								
Krishnegowda Layout 1st Main	Rmt	1	50.00					
K K Road Near Masjid		1	50.00			50.00		
Buvaneshwari nagar 3rd Main		1	50.00			50.00		
						50.00		
						150.00	**156.00**	**23400.00**

Assistant Engineer
Ward 15
24/05/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Digging of trench of 0.6m deep x 0.50 mtr wide refilling the trench to the required ground level and consolidating etc., complete.(As per Civil SR KSRB I-2, P-7) cutting road surface in hard soil **(Ele SR 2019-20 P-NO41/ I/NO 6.6.2)**								
Krishnegowda Layout 1st Main	Rmt	1	50.00					
K K Road Near Masjid		1	50.00			50.00		
Buvaneshwari nagar 3rd Main		1	50.00			50.00		
						50.00		
						150.00	**106.08**	**15912.00**

Assistant Engineer
Ward 15
01/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Labour charges for laying of 1.1 KV class UG cable in existing trench GI pipe / stoneware pipe / on wall / on pole as required.6 sqmm to 16 sqmm. **(Ele SR 2019-20 P-NO41/ I/NO 6.5.1)**								
Krishnegowda Layout 1st Main	Rmt	1	45.00			45.00		
K K Road Near Masjid		1	45.00			45.00		
Buvaneshwari nagar 3rd Main		1	45.00			45.00		
						135.00	**19.01**	**2566.00**

Assistant Engineer
Ward 15
01/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Supplying and fixing L.T. cast Iron pot heads suitable for 1.1 KV class UG cable filled with necessary bitumen/insulating compound complete with terminals, clamps, bolts, nuts and washers etc.**(Ele SR 2019-20 P-NO42/ I/NO 6.10.2)**								
Krishnegowda Layout 1st Main	No	1	3.00			3.00		
K K Road Near Masjid		1	3.00			3.00		
Buvaneshwari nagar 3rd Main		1	3.00			3.00		
						9.00	**280.80**	**2527.00**

Assistant Engineer
Ward 15
02/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Scanned with CamScanner

No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
	Supplying & fixing of Porcelain fuse channel with cut out on existing wooden/panel using necessary nuts, bolts and washers.**(Ele SR 2019-20 P. NO25/ I/NO 5.7.2)**								
	Krishnegowda Layout 1st Main	No	1	3.00			3.00		
	K K Road Near Masjid		1	3.00			3.00		
	Buvaneshwari nagar 3rd Main		1	3.00			3.00		
							9.00	**180.96**	**1629.00**

Assistant Engineer
Ward 15
02/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

	Cutting of road surface for pipeline trenches and disposing of the excavated stuff as directed including barricading, danger lighting etc.in the following classification.(RDWS SR 2019-20Pg No.08 I.No.2.26)Cutting Asphalt Road Surface **(SR RDWS&S 2019-20, Pg No.14 I.No.2.26.2)**								
	Krishnegowda Layout 1st Main	Cum	1	30.00	0.6	0.15	2.70		
	K K Road Near Masjid		1	30.00	0.6	0.15	2.70		
	Buvaneshwari nagar 3rd Main		1	30.00	0.6	0.15	2.70		
							8.10	**563.68**	**4566.00**

Assistant Engineer
Ward 15
03/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

	Cutting of road surface for pipeline trenches and disposing of the excavated stuff as directed including barricading, danger lighting etc.in the following classification.Cutting in cement concrete road Surface **(SR RDWS&S 2019-20, Pg No.14 I.No.2.26.3)**								
	Krishnegowda Layout 1st Main	Cum	1	30.00	0.3	0.15	1.35		
	K K Road Near Masjid		1	30.00	0.3	0.15	1.35		
	Buvaneshwari nagar 3rd Main		1	30.00	0.3	0.15	1.35		
							4.05	**1150.24**	**4658.00**

Assistant Engineer
Ward 15
03/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Scanned with CamScanner

No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
	Earthwork excavation for pipeline trenches including depositing on bank upto a lead of 50 mtrs and depth up to 2.00 mtrs. Including shoring and strutting, danger lighting and using sight rails and boning rods at every 100 mtrs. Wherever necessary as directed in the following strata. (Manual Means) in ordinary soil **(SR RDWS&S 2019-20, Pg No.13 I.No.2.22.1)**								
	Krishnegowda Layout 1st Main	Cum	7	30.00	0.3	0.75	47.25		
	1st Cross		1	28.00	0.3	0.75	6.30		
	K K Road		3	30.00	0.3	0.75	20.25		
	3rd Cross		2	30.00	0.3	0.75	13.50		
	4th Cross		2	30.00	0.3	0.75	13.50		
	Masjid Road		1	28.00	0.3	0.75	6.30		
	Buvaneshwari nagar 4th Main		7	30.00	0.3	0.75	47.25		
			1	23.00	0.3	0.75	5.18		
							159.53	**272.48**	**43467.00**

Assistant Engineer
Ward 15
03/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

	Providing and installing at site of work P.V.C. pipes including cost of pipes and specials and labour, including lowering into trenches, laying true to line, level and perfect linking at joints leak proof including jointing of approved type with all labour charges and all lift charges, handling charges including encasing the pipe around to a depth not less than 15 cms with gravel or selected earth available from the excavation etc. complete. **(RDWS SR 2019-20Pg No.89 I.No.10.01.2)(a) 63mm** dia 6kg/cm2								
	Krishnegowda Layout 1st Main	Rmt	7	30.00			210.00		
	1st Cross		1	28.00			28.00		
	K K Road		3	30.00			90.00		
	3rd Cross		2	30.00			60.00		
	4th Cross		2	30.00			60.00		
	Masjid Road		1	28.00			28.00		
	Buvaneshwari nagar 4th Main		7	30.00			210.00		
			1	23.00			23.00		
							709.00	**161.20**	**114291.00**

Assistant Engineer
Ward 15
07/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Scanned with CamScanner

No	Description	Unit	Nos	L	B	D	Qty.	Rate	Amount
	Refilling the basement and pipeline trenches with selected available earth from trench excavation including watering, Consolidation in layers of 15 cm thick including disposing of the surplus earth with all lead & lifts. (Compacting with vibro roller) **(SR RDWS&S 2019-20, Pg No.14**								
	Krishnegowda Layout 1st Main	Cum	7	30.00	0.3	0.75	47.25		
	1st Cross		1	28.00	0.3	0.75	6.30		
	K K Road		3	30.00	0.3	0.75	20.25		
	3rd Cross		2	30.00	0.3	0.75	13.50		
	4th Cross		2	30.00	0.3	0.75	13.50		
	Masjid Road		1	28.00	0.3	0.75	6.30		
	Buvaneshwari nagar 4th Main		7	30.00	0.3	0.75	47.25		
			1	23.00	0.3	0.75	5.18		
							159.53	**107.12**	**17088.00**

Assistant Engineer
Ward 15
10/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

	Supply and delivery at site of brand new best make gate valve as per IS 778/1984 with ISI Mark and as per its latest amendments **(SR RDWS&S 2019-20, Pg No.158 .I.12.05) a) 50mm dia**								
	Krishnegowda Layout 1st Main	Each	1	8.00			8.00		
	K K Road Near Masjid		1	6.00			6.00		
	Buvaneshwari nagar 3rd Main		1	6.00			6.00		
							20.00	**1237.60**	**24752.00**

Assistant Engineer
Ward 15
15/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

	Bescom charges								
		each	3				**3.00**	**19500.00**	**58500.00**
								Sub Total	**3167642.00**
								GST Charges 12%	**380117.00**
								Grand Total	**3547759.00**

Assistant Engineer
Ward 15
21/06/21

Assistant Executive Engineer
T Dasarahalli Sub Division, BBMP

Scanned with CamScanner

Name of work :- Providing Sinking of borewell drilling & pumpsets in Dasarahalli ward No-15.

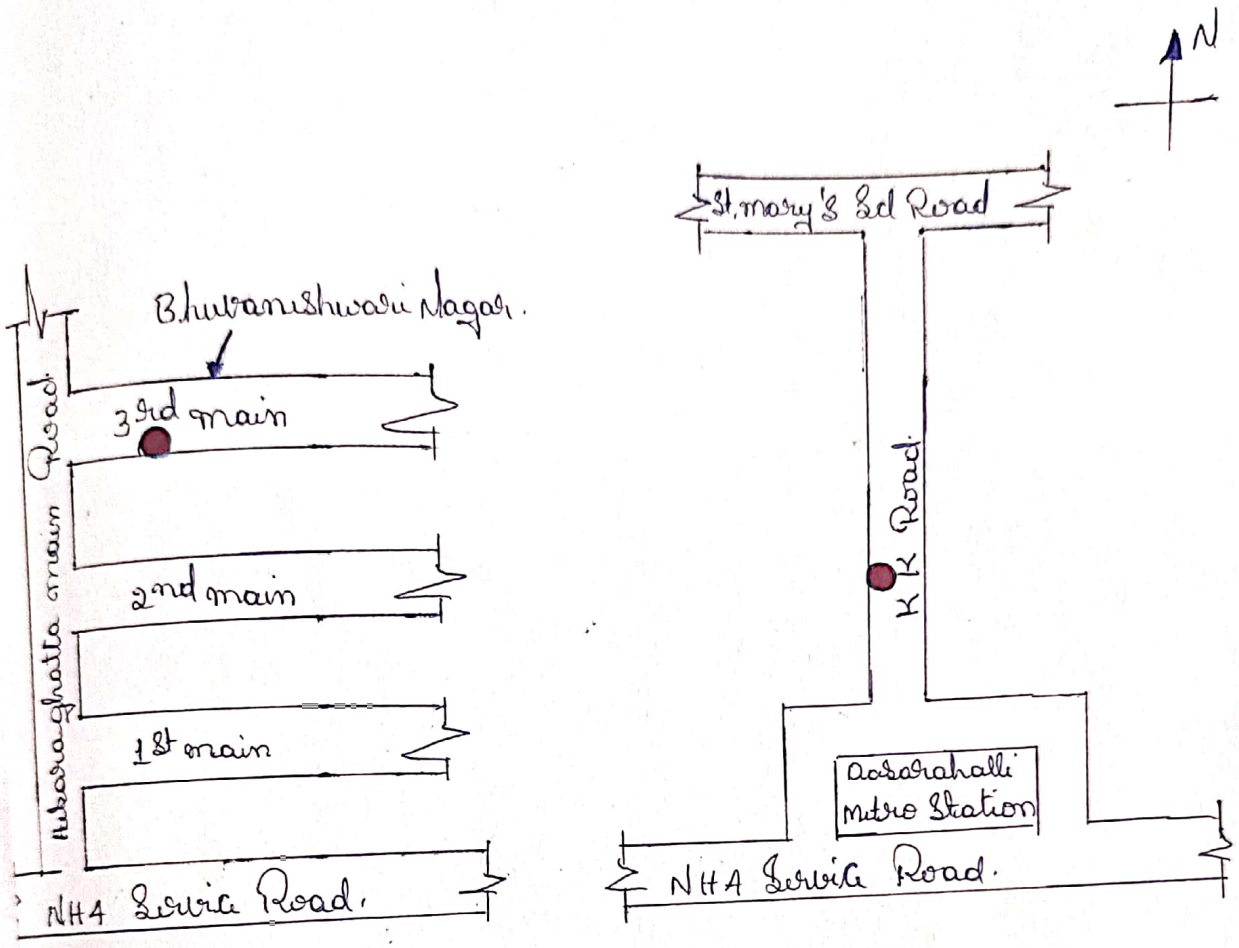

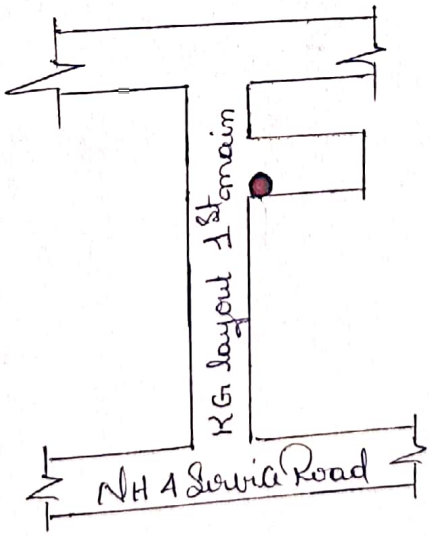

INDEX

Work Spot of Borewell

AE-15
21-06-21

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಜ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner
